




UNDER CONSTRUCTION

Ludington Area Schools MSHS Additions and Renovations




Project Duration is 33% Complete



MS Sitework



HS Main Entrance

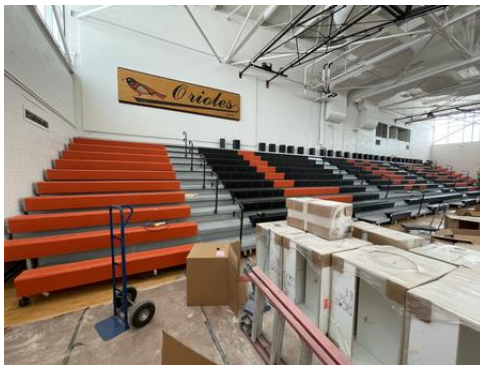

Hawley Gymnasium Bleachers

WORK IN PROGRESS

This Month

- Pave bus loop and complete HS staff lot
- Install landscaping and grass seed
- Complete polished concrete floors
- Demo existing MS art room
- Install finishes in classrooms to be used in September
- Obtain MEP and building inspections

Next Month

- Occupy phase 2 construction areas
- Install underground plumbing
- Build new locker room walls and new cafeteria walls
- Continue demolition throughout phase 2

PROJECT MANAGEMENT UPDATE

Safety

- This month's Safety Goal focuses on proper excavations

Schedule

- The project is on schedule


Other Progress

- Oriole field artificial turf turnover 8/7
- Team room construction to begin early September



UNDER CONSTRUCTION

Ludington Area Schools MSHS Additions and Renovations



HS Collaboration Room



Bathroom Near Band and Choir



Band Room



HS Science Room



MS New Classroom



Site Work Near Bus Loop
