




# UNDER CONSTRUCTION

## Ludington Area Schools MSHS Additions and Renovations




Project is 5% Complete



HS Student Parking Prep



HS Student Parking Prep

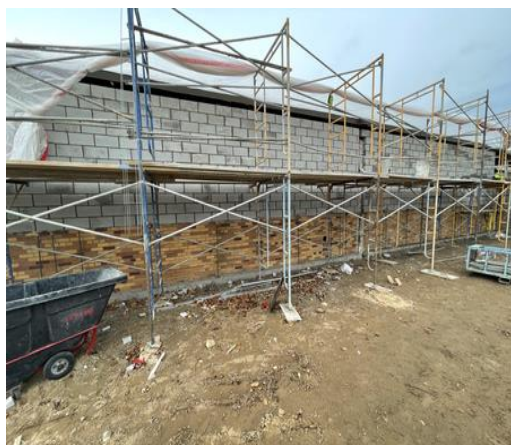

HS Office South Wall

### WORK IN PROGRESS

#### This Month

- Site clearing and digging for foundations at MS
- Install underground plumbing and electrical at additions
- Finish curbs and pave student lot
- Lay block walls at HS office and classroom
- Begin pouring foundations at MS

#### Next Month

- Pour floor at HS additions (pending weather)
- Install water detention tanks at HS lot
- Erect steel at HS
- Begin block work at MS

### PROJECT MANAGEMENT UPDATE

#### Safety

- This month's Safety Goal focuses on maintaining a barrier between construction and school activities.

#### Schedule

- The project is on schedule


#### Other Progress

- Oriole Field improvements is bidding in December.
- Establishing power shutdown plans for summer 2023.



# UNDER CONSTRUCTION

## Ludington Area Schools MSHS Additions and Renovations



Pouring Column Pads



Foundation Wall at Office



Classroom Addition Foundation Wall



Prep Work for MS Addition



Pouring Column Pads



Dewatering in Place for Foundations
